


CONTRACT FOR CONSULTANCY SERVICES  
No. 08-389/3 DATED 16.01.2023

SUPERVISION AND LEGAL TRANSACTION ADVISOR FOR  
CONSTRUCTION OF CORRIDOR VIII AND CORRIDOR X-d

## EXECUTIVE SUMMARY OF REPORT

for period 01.11.2023 – 31.12.2023



PUBLIC ENTERPRISE FOR STATE ROADS

NOVEMBER-DECEMBER 2023

---

### ENGINEER

GROUP OF BIDDERS:

*IRD ENGINEERING S.R.L – ROME (IT)*

*EPTISA SERVICIOS DE INGENIERIA S.L (ES)*

*ELEKTRA SOLUTIONS DOOEL - SKOPJE (MK)*

*EURO CONSULT DOO - SKOPJE (MK)*

---

1- Project Parties:

---

**Contractor:**

BECHTEL ENKA UK 2 Limited



**Employer:**

Public Enterprise for State Roads and the Ministry of Transport and  
Communications on behalf of the Government of the Republic of North  
Macedonia



**Engineer:**

IRD Engineering s.r.l – Rome (IT) – JV leader JV members:  
EPTISA Servicios de ingenieria s.l; ELECTRA SOLUTIONS DOOEL  
Skopje and EURO CONSULTING DOO  
Skopje



## 2- Project Overview and Key Quantities:


Corridor VIII and X-d project consists of four (4) sections 109 km in total crossing highways, railways and, Vardar and Black Drin Rivers along the route.

Corridor VIII is a key component of the Indicative extension of the TEN-T Core and Comprehensive Network to the Western Balkans, connecting the Adriatic Sea and the Black Sea through Albania, North Macedonia, and Bulgaria. Per project scope, Tetovo – Gostivar - Bukojcani and Trebenista – Struga – Kjafasan Motorway sections (Section 1, 2 and 3) will be built.

Corridor X-d is a also part of Indicative extension of the TEN-T Core and Comprehensive Network to the Western Balkans connecting North Macedonia and Greece. Per project scope, Prilep- Bitola section (Section 4) will be built.

These Corridors are connecting the Republic of North Macedonia with the regional infrastructure and ports in Albania, Bulgaria, and Greece.

Below is a picture of the indicative extension of the TEN-T Core and Comprehensive Networks in Western Balkans as provided for by the Commission Delegated Regulation (EU) 2016/7581- Annex I.1

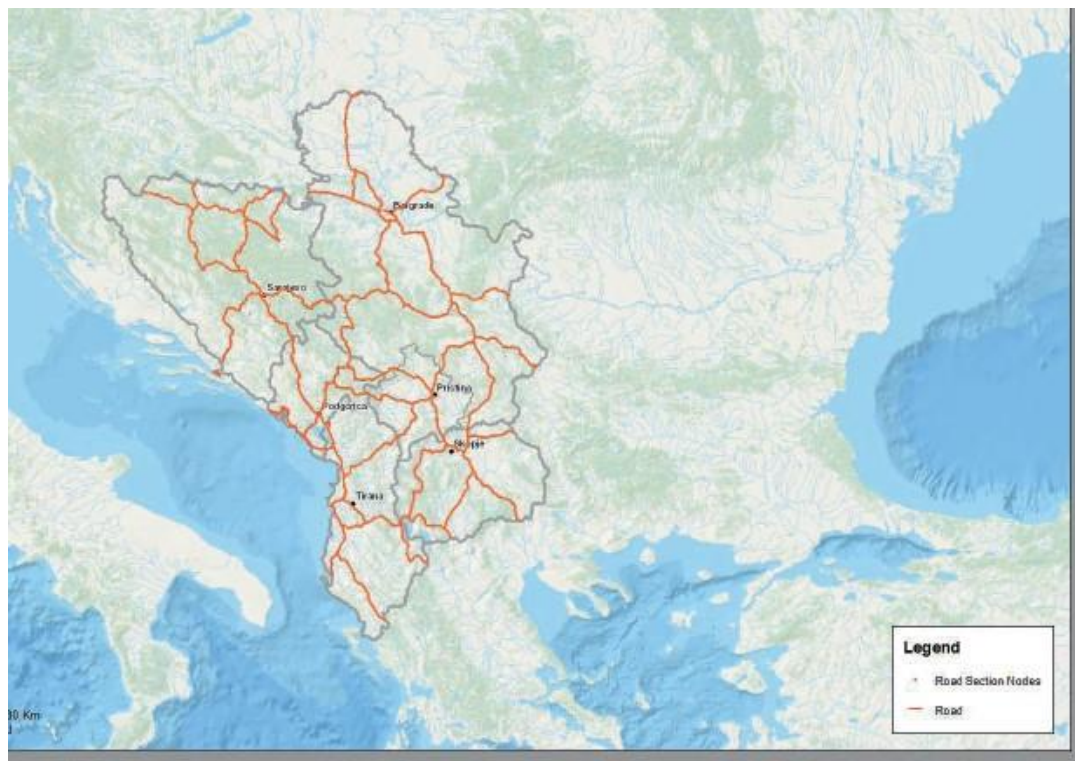


*Indicative Extension of TEN-T Core and Comprehensive Road Network to the Western Balkans*



REPUBLIC OF NORTH MACEDONIA

INDICATIVE ALIGNMENT PLAN VIEW

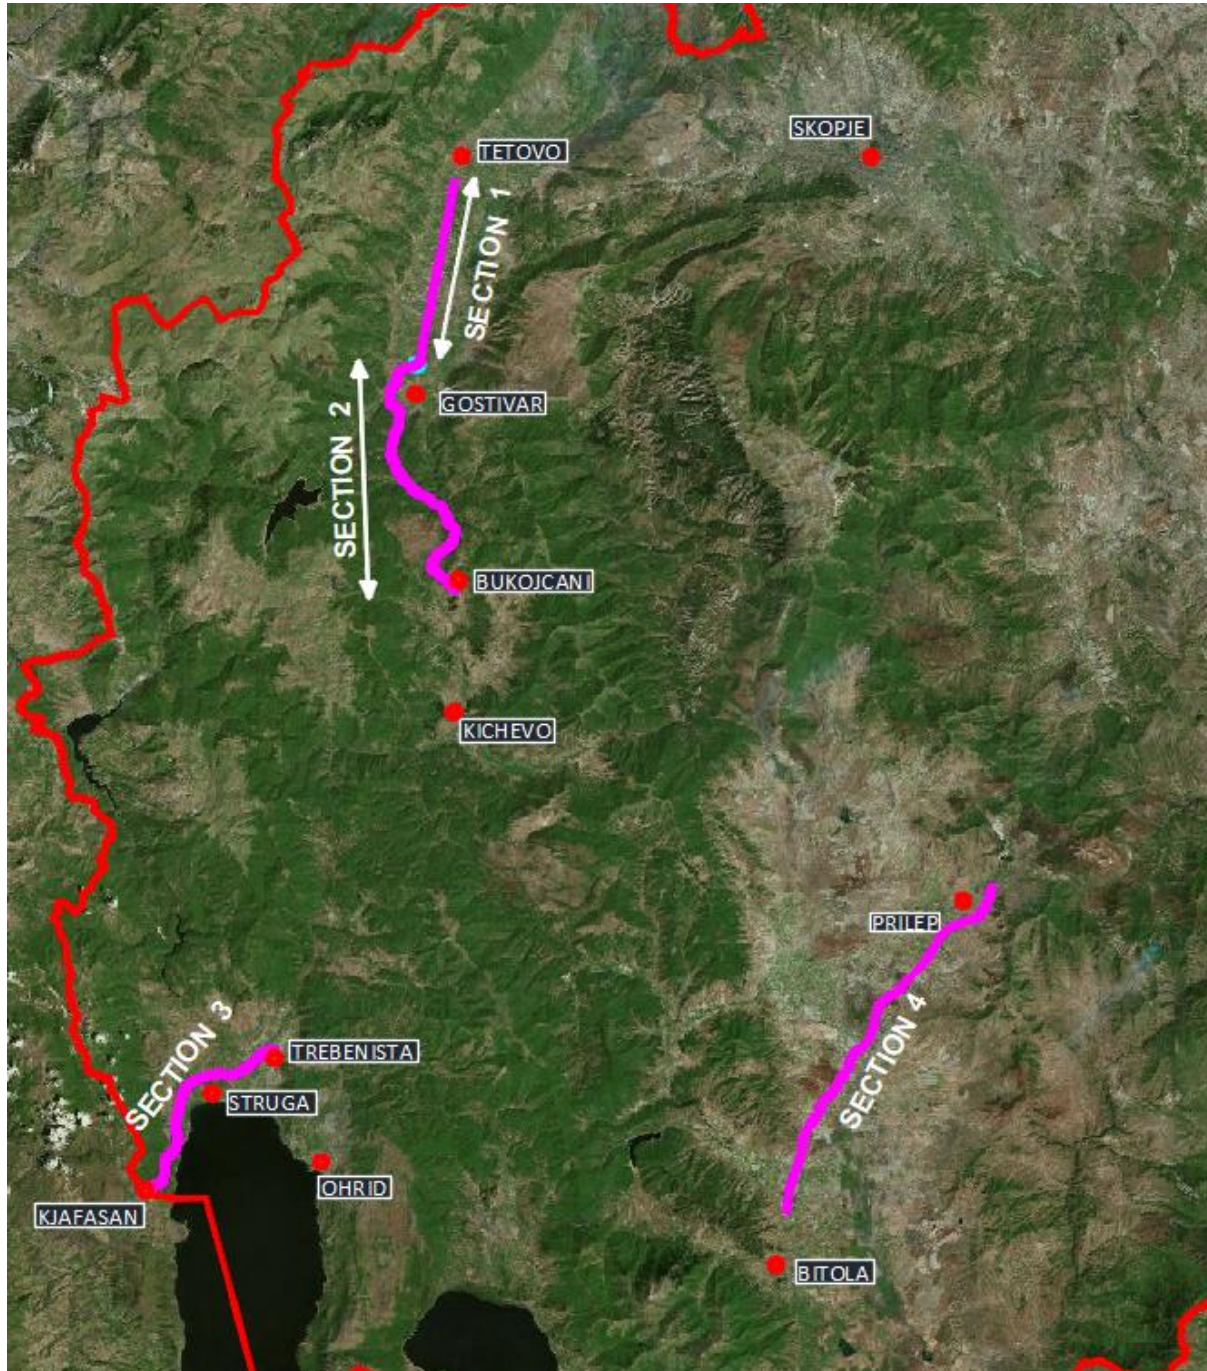

**REPUBLIC OF NORTH MACEDONIA**

**GENERAL PROJECT OVERVIEW**

<b>Construction Contract:</b>	Construction of Corridor 8: Tetovo – Gostivar - Bukojcani and Trebenista – Struga - Kjafasan Motorway section and Corridor 10-d: Prilep – Bitola Motorway section		
<b>Construction Contract Number:</b>	No. 09-2234/1 dated 08.03.2023		
<b>Name:</b>	Public Enterprise for State Roads and the Ministry of Transport and Communications on behalf of the Government of the Republic of North Macedonia	Bechtel Enka UK 2 Limited operating through BECHTEL ENKA UK 2 LIMITED-Branch Office in North Macedonia Skopje	IRD Engineering s.r.l – Rome (IT) – JV leader JV members: EPTISA Servicios de ingenieria s.l; ELECTRA SOLUTIONS DOOEL Skopje and EURO CONSULTING DOO Skopje
<b>Role:</b>	Collectively called the “Employer”	Contractor	Engineer
<b>Purpose of Construction Contract:</b>	Provision of Construction Services in the capacity of the Contractor to execute and complete the Works in accordance with the Contract.		

REPUBLIC OF NORTH MACEDONIA



The Project's major estimated quantities are shown below. As part of the Work scope, design and design related work is ongoing. Below mentioned quantities shall be subject to change in accordance with project technical requirements.

<b>Total Length (km)</b>	109 km
<b>Total Number of Underpasses (ea)</b>	24
<b>Total Number of Overpasses (ea)</b>	34
<b>Total Length of Bridges (m)</b>	4,500m
<b>Total Excavation (m<sup>3</sup>)</b>	21 million m <sup>3</sup>
<b>Total Fill (m<sup>3</sup>)</b>	10 million m <sup>3</sup>
<b>Total Concrete (m<sup>3</sup>)</b>	620,000 m <sup>3</sup>
<b>Total Subbase (m<sup>3</sup>)</b>	1.2 million m <sup>3</sup>
<b>Total Asphalt (ton)</b>	1.1 million ton

### 3- Work Progress:

In the period of November and December 2023, Contractor continued to perform works mainly for expropriation design, geotechnical investigation works, other previous activities and motorway specifications.

Overall Progress of the Project is shown below:

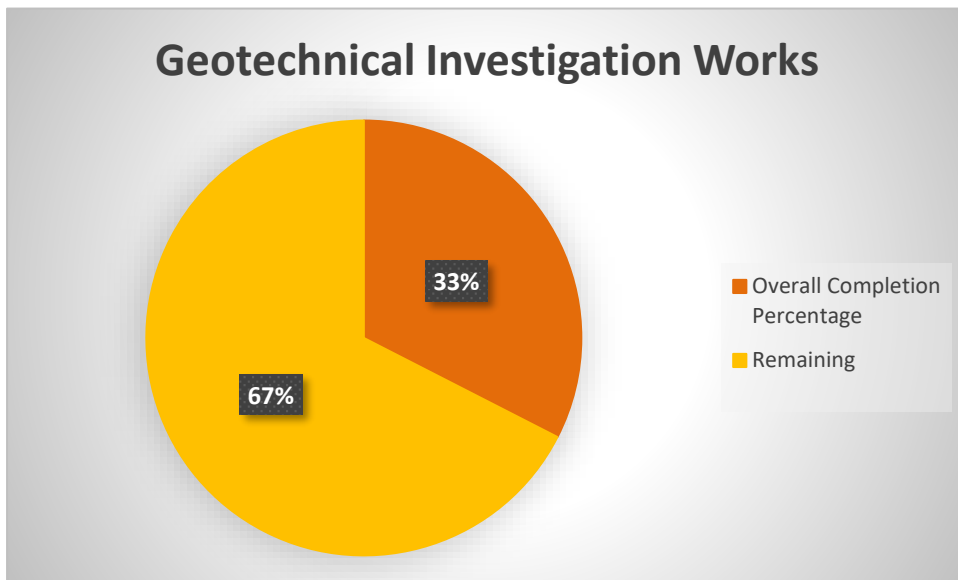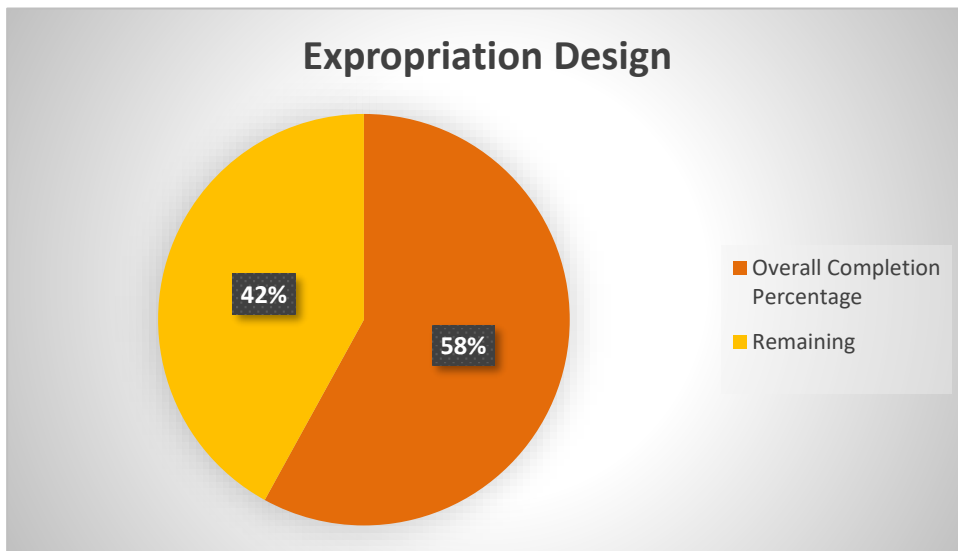

4- Financial Progress of the Project:

Financial transaction between Ministry of Transport & Communications and Public Enterprise State Roads under road infrastructure financing program is listed below:

Date	Payer Name	Recipient Name	Amount (MKD)
26.04.2023	Ministry of Transport & Communications	Public Enterprise for State Roads	7.254.000.000
23.06.2023	Ministry of Transport & Communications	Public Enterprise for State Roads	3.280.000.000
28.07.2023	Ministry of Transport & Communications	Public Enterprise for State Roads	443.602.000
10.08.2023	Ministry of Transport & Communications	Public Enterprise for State Roads	209.927.500
02.10.2023	Ministry of Transport & Communications	Public Enterprise for State Roads	216.308.513
09.11.2023	Ministry of Transport & Communications	Public Enterprise for State Roads	223.596.680
15.12.2023	Ministry of Transport & Communications	Public Enterprise for State Roads	245.606.294
28.12.2023	Ministry of Transport & Communications	Public Enterprise for State Roads	669.225.176
28.12.2023	Ministry of Transport & Communications	Public Enterprise for State Roads	261.862.793
29.12.2023	Ministry of Transport & Communications	Public Enterprise for State Roads	1.695.871.044
